



LECTURE 4

Overview of the Scrum Process


COEN / ELEC 390

Acknowledgement

- The content of these slides is based on Chapters 2 and 3 of the textbook :

Essential Scrum, A Practical Guide to the Most Popular Agile Process
Kenneth S. Rubin, Addison-Wesley, 2013.

The Scrum Framework

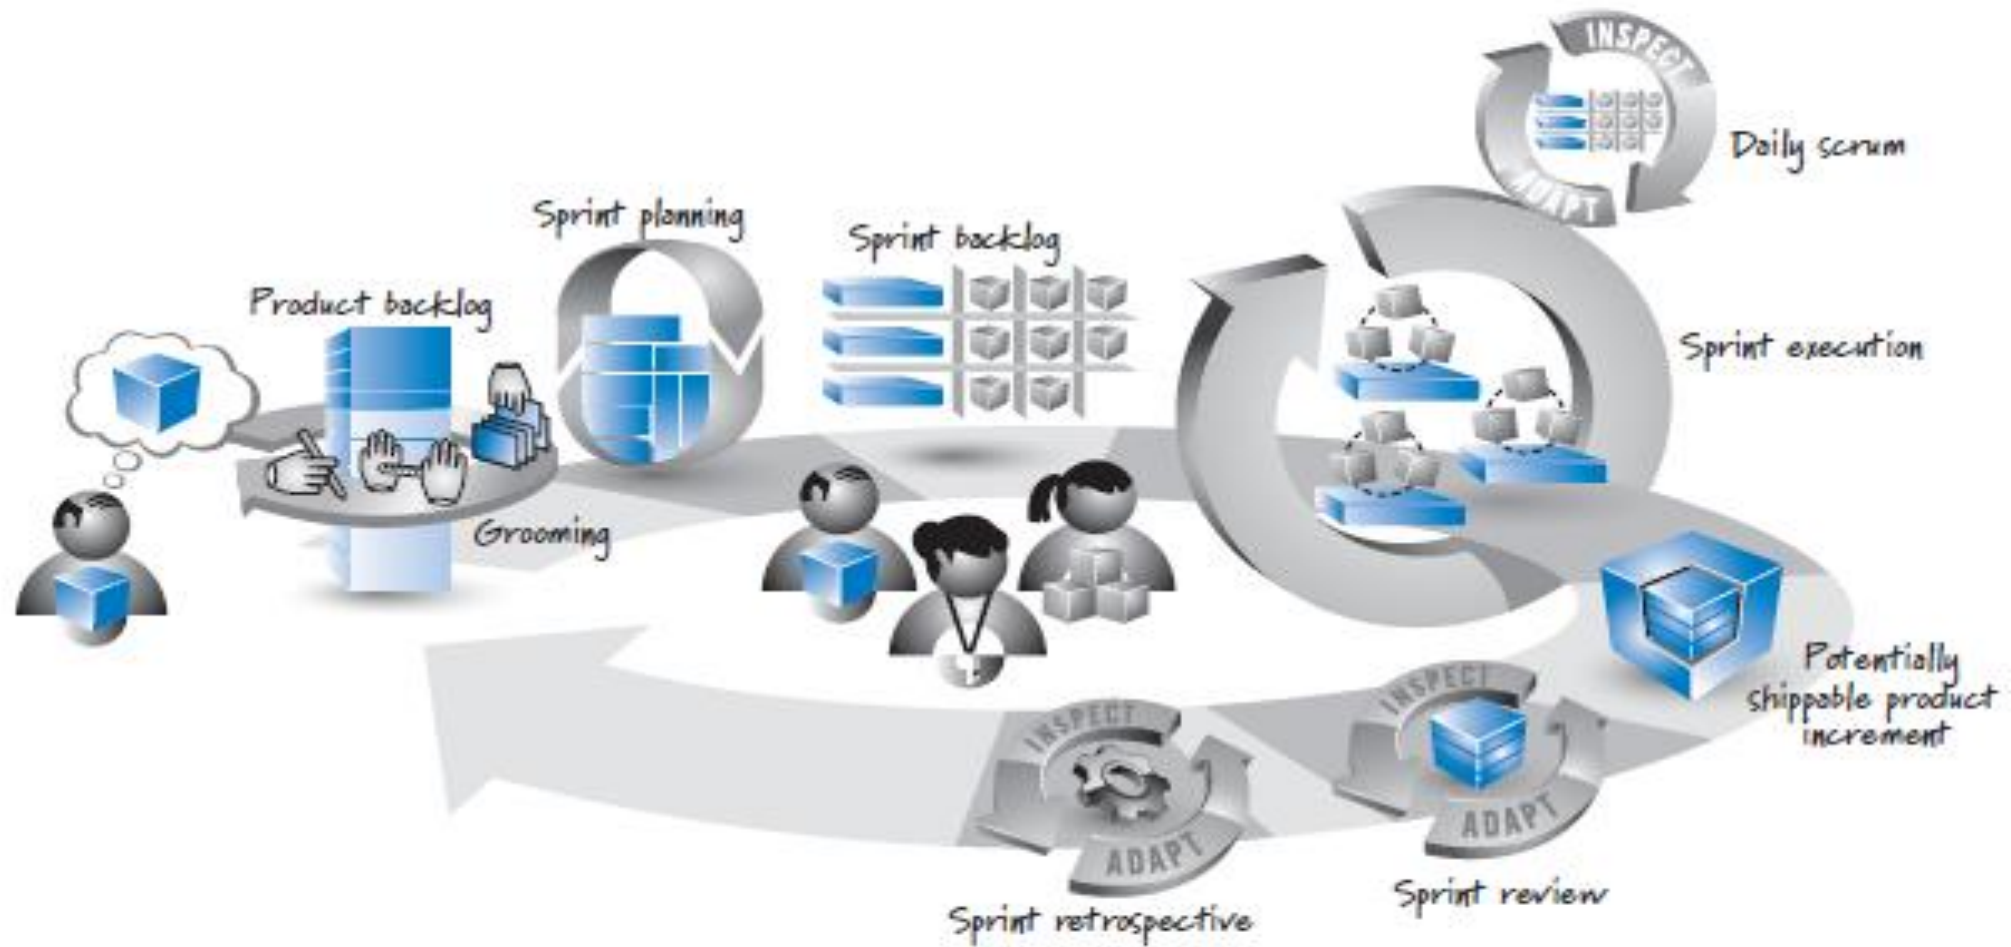

Roles and Responsibilities

Product Owner

- Central point of product leadership
- Responsible for what gets built and when
- Presents a clear vision
- Ensures the most valuable work is being done

Scrum Master

- Oversees the implementation of Scrum
- Acts as a facilitator of the process
- Removes obstacles


Dev Team

- Cross-functional team of people who designs, builds and tests the product
- A self-organized team
- Small in size but can be organized into several teams


The Concept of Sprints

- Scrum is an iterative and incremental process
- Sprints are iterations – the end of each sprint should lead to a release
- Sprints are time-boxed with a fixed start and end dates
- A new sprint immediately follows the completion of the previous sprint
- No goal-altering changes in scope or personnel during a sprint

Product Backlog

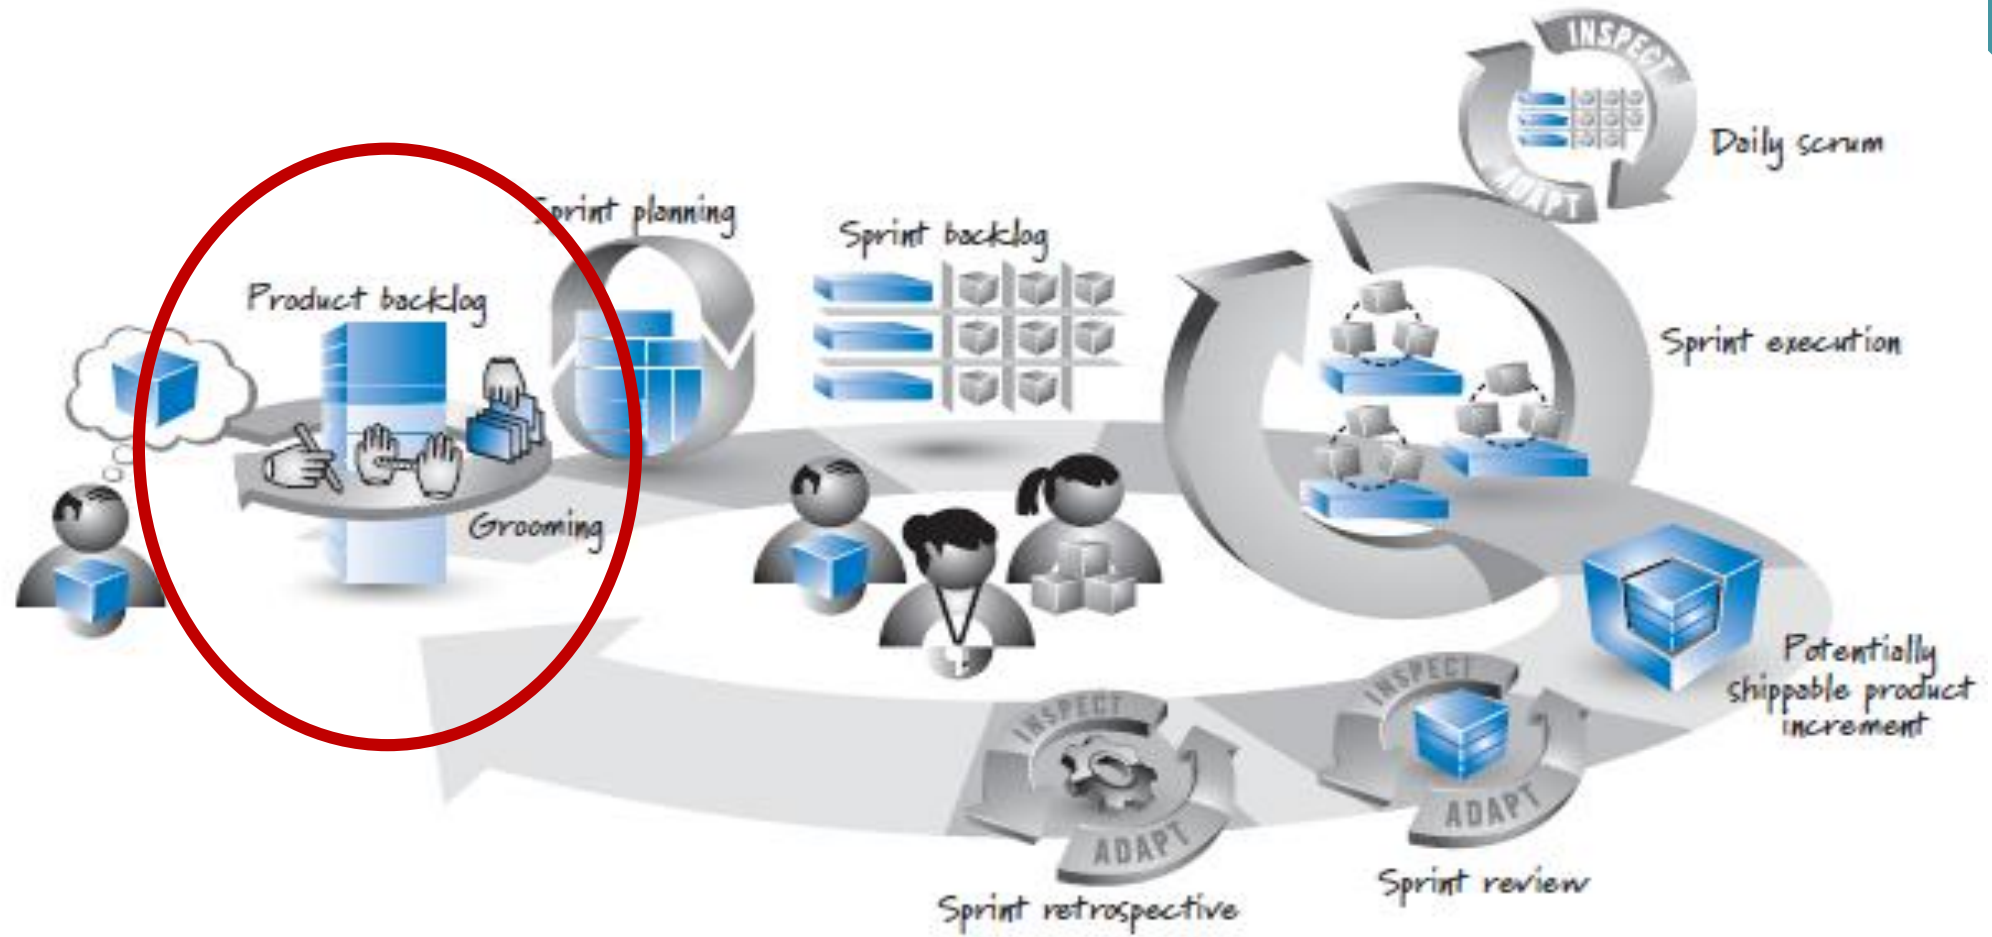

Product Backlog

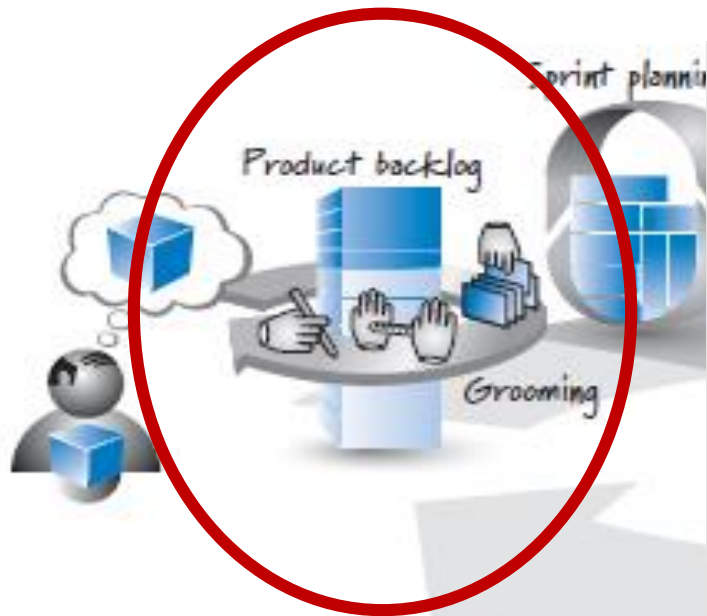


- A set of features that need to be implemented
- The activity of creating and refining product backlog items, estimating them, and prioritizing them is known as grooming
- Before prioritizing, we need to know the size of each item, as size equates to cost




Product Backlog (cont.)

- We always do the most valuable work first
- The product owner is responsible for determining, managing & communicating the sequence of this work
- The product owner collaborates with their team and internal and external stakeholders to gather and define the product backlog items
- The product backlog is a constantly evolving artifact

Sprint Planning

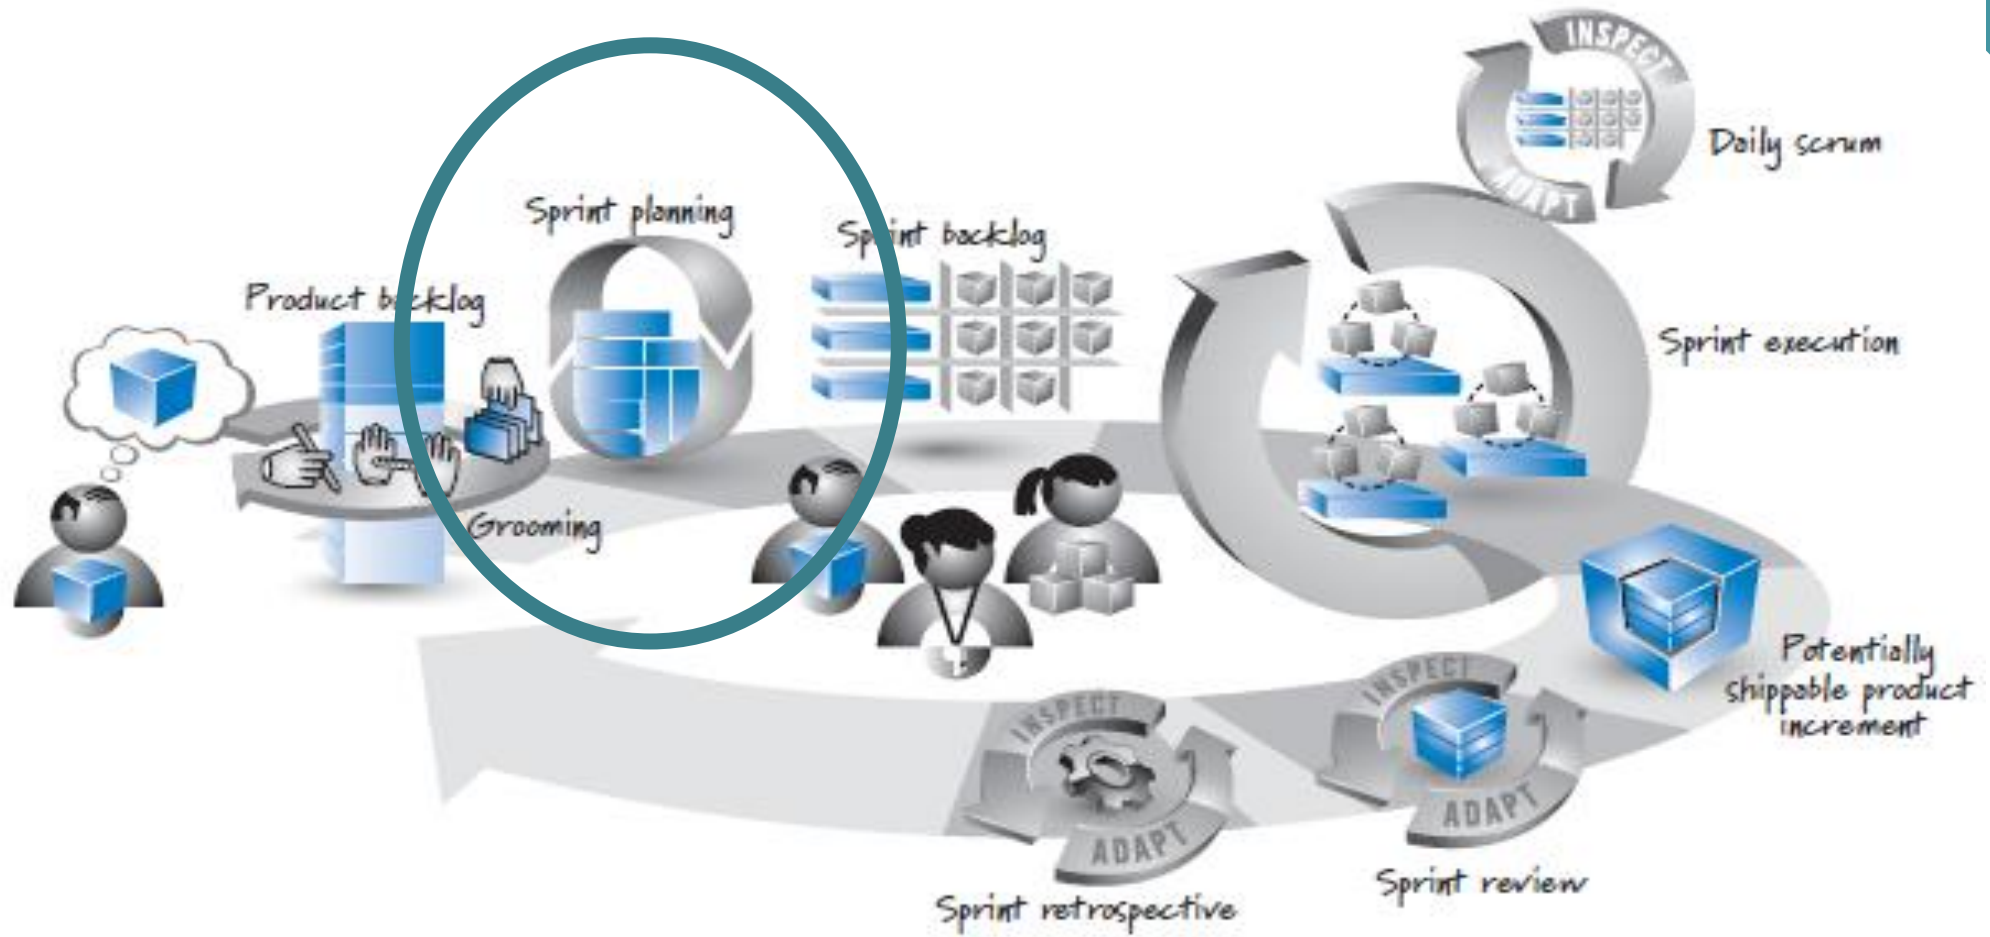


Sprint Planning

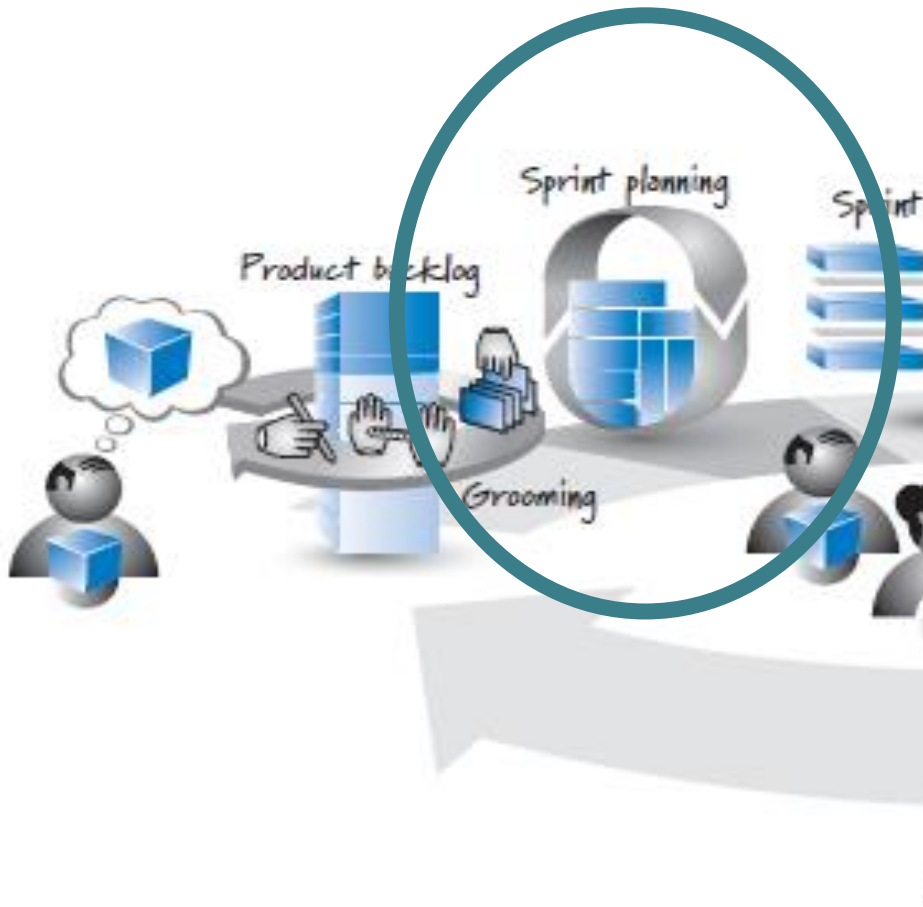


- The product owner and development team agree on a sprint goal
- Using this goal, the development team reviews the PB and determines the highest priority items (features) that the team can do in the upcoming sprint while working at a sustainable pace
- Features are broken into tasks, and together (features & tasks) form a second backlog called the sprint backlog
- A 1-week sprint should not take more than 2 hours to plan
- Make sure that the capacity of the team is not exceeded by the amount of ideal hours required

Sprint Backlog

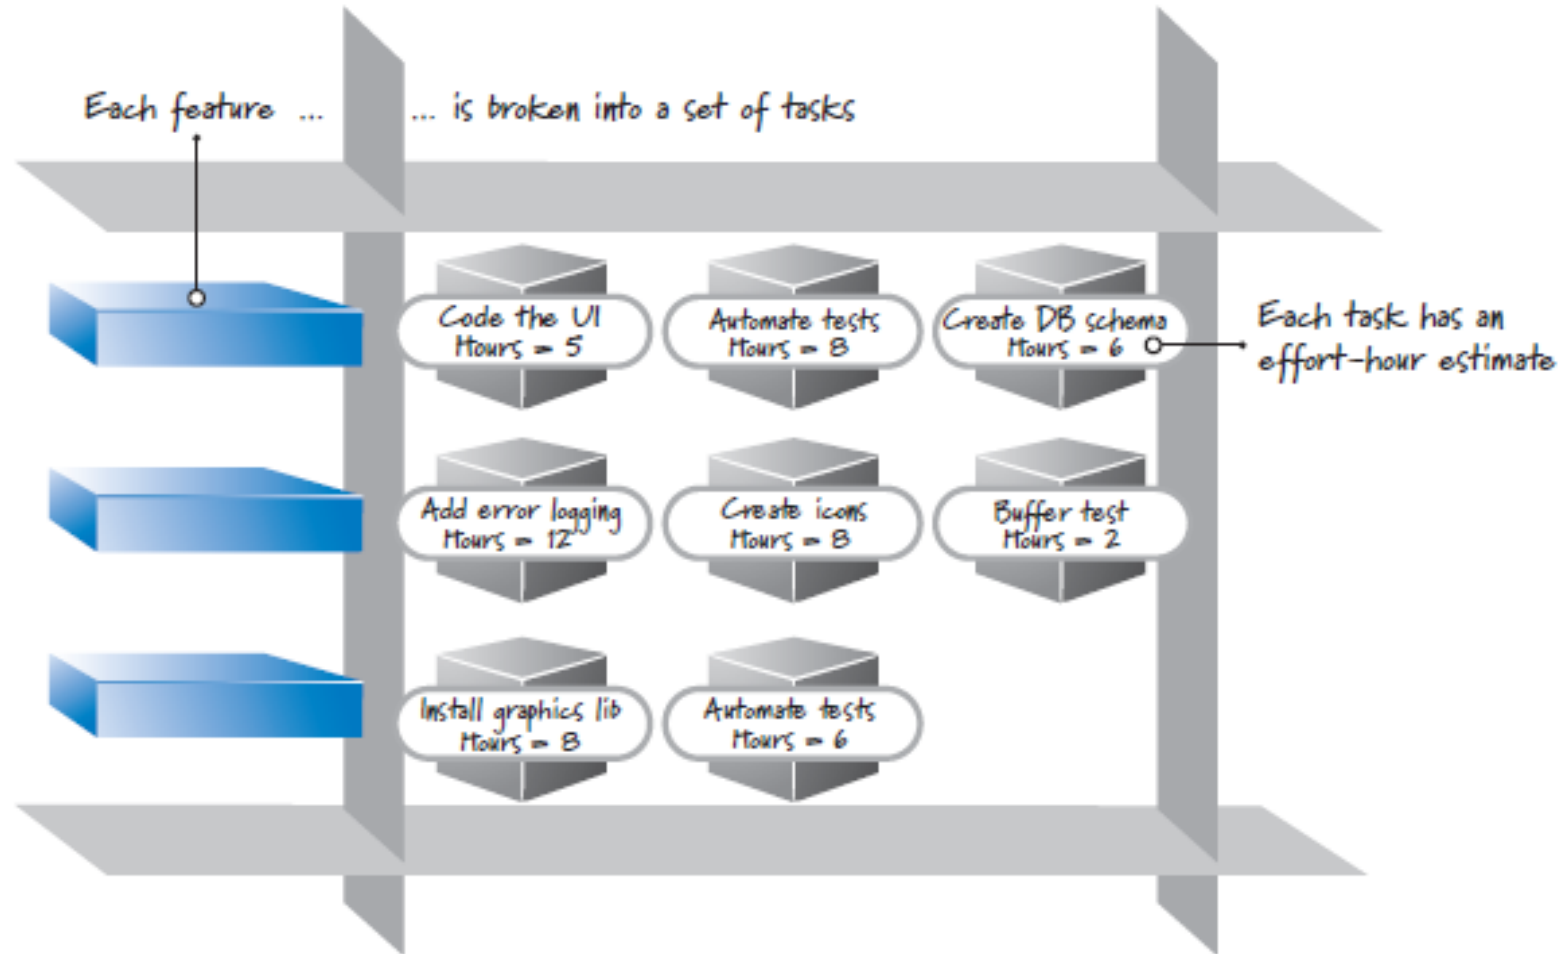


Sprint Planning

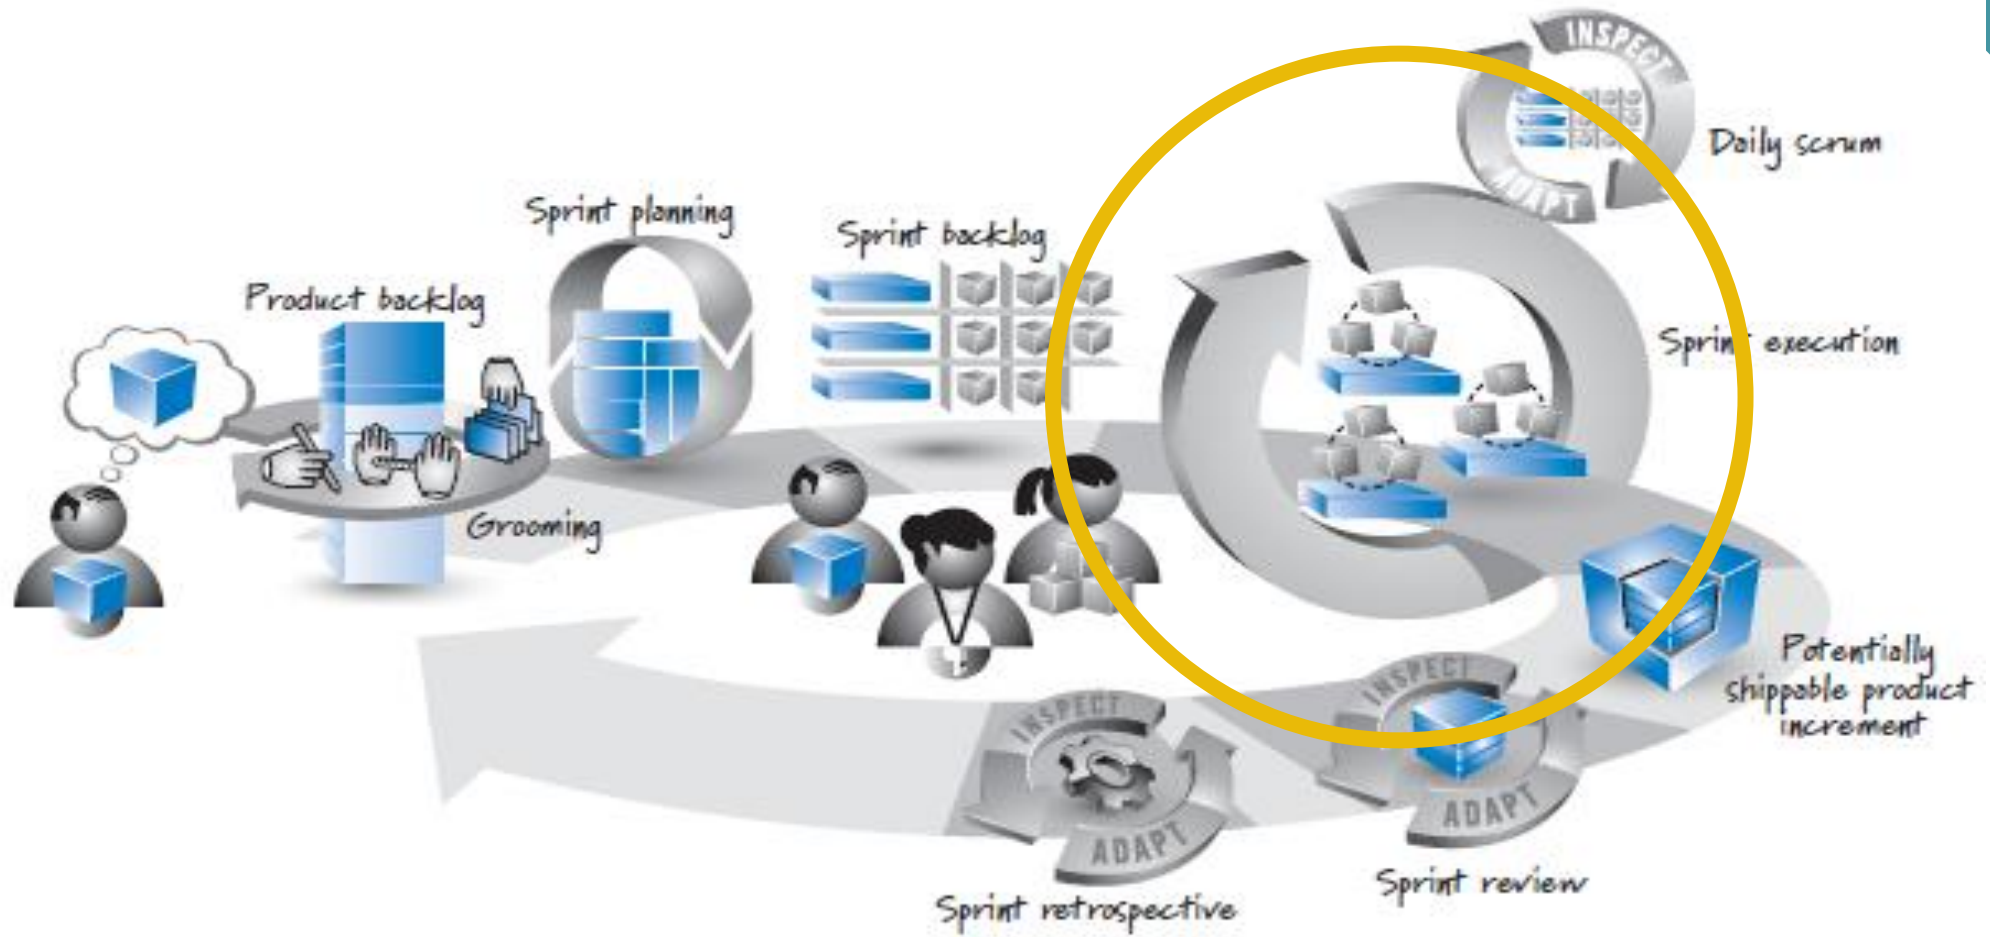


Sprint Execution

- The development team, guided by the ScrumMaster's coaching, performs all of the task-level work necessary to get the features done
- Nobody tells the development team in what order or how to do the task-level work in the sprint backlog

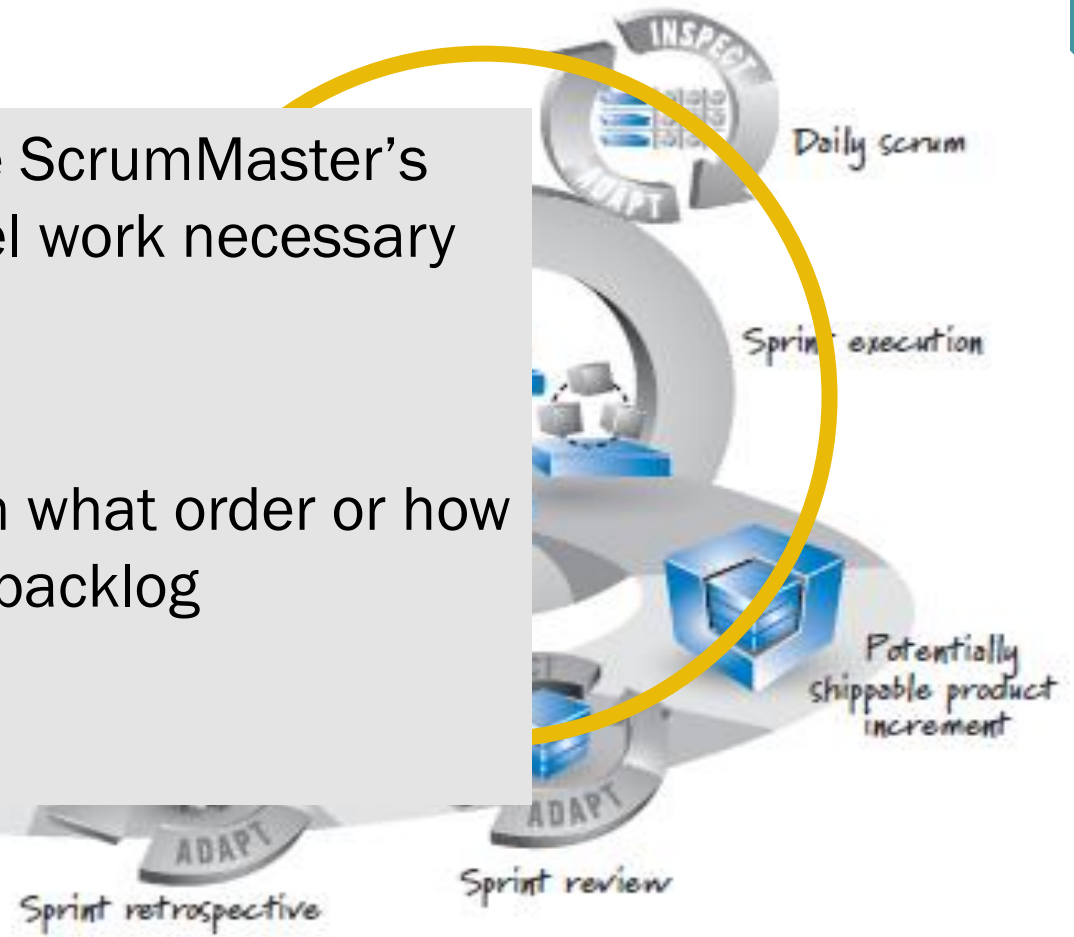


Daily Scrum

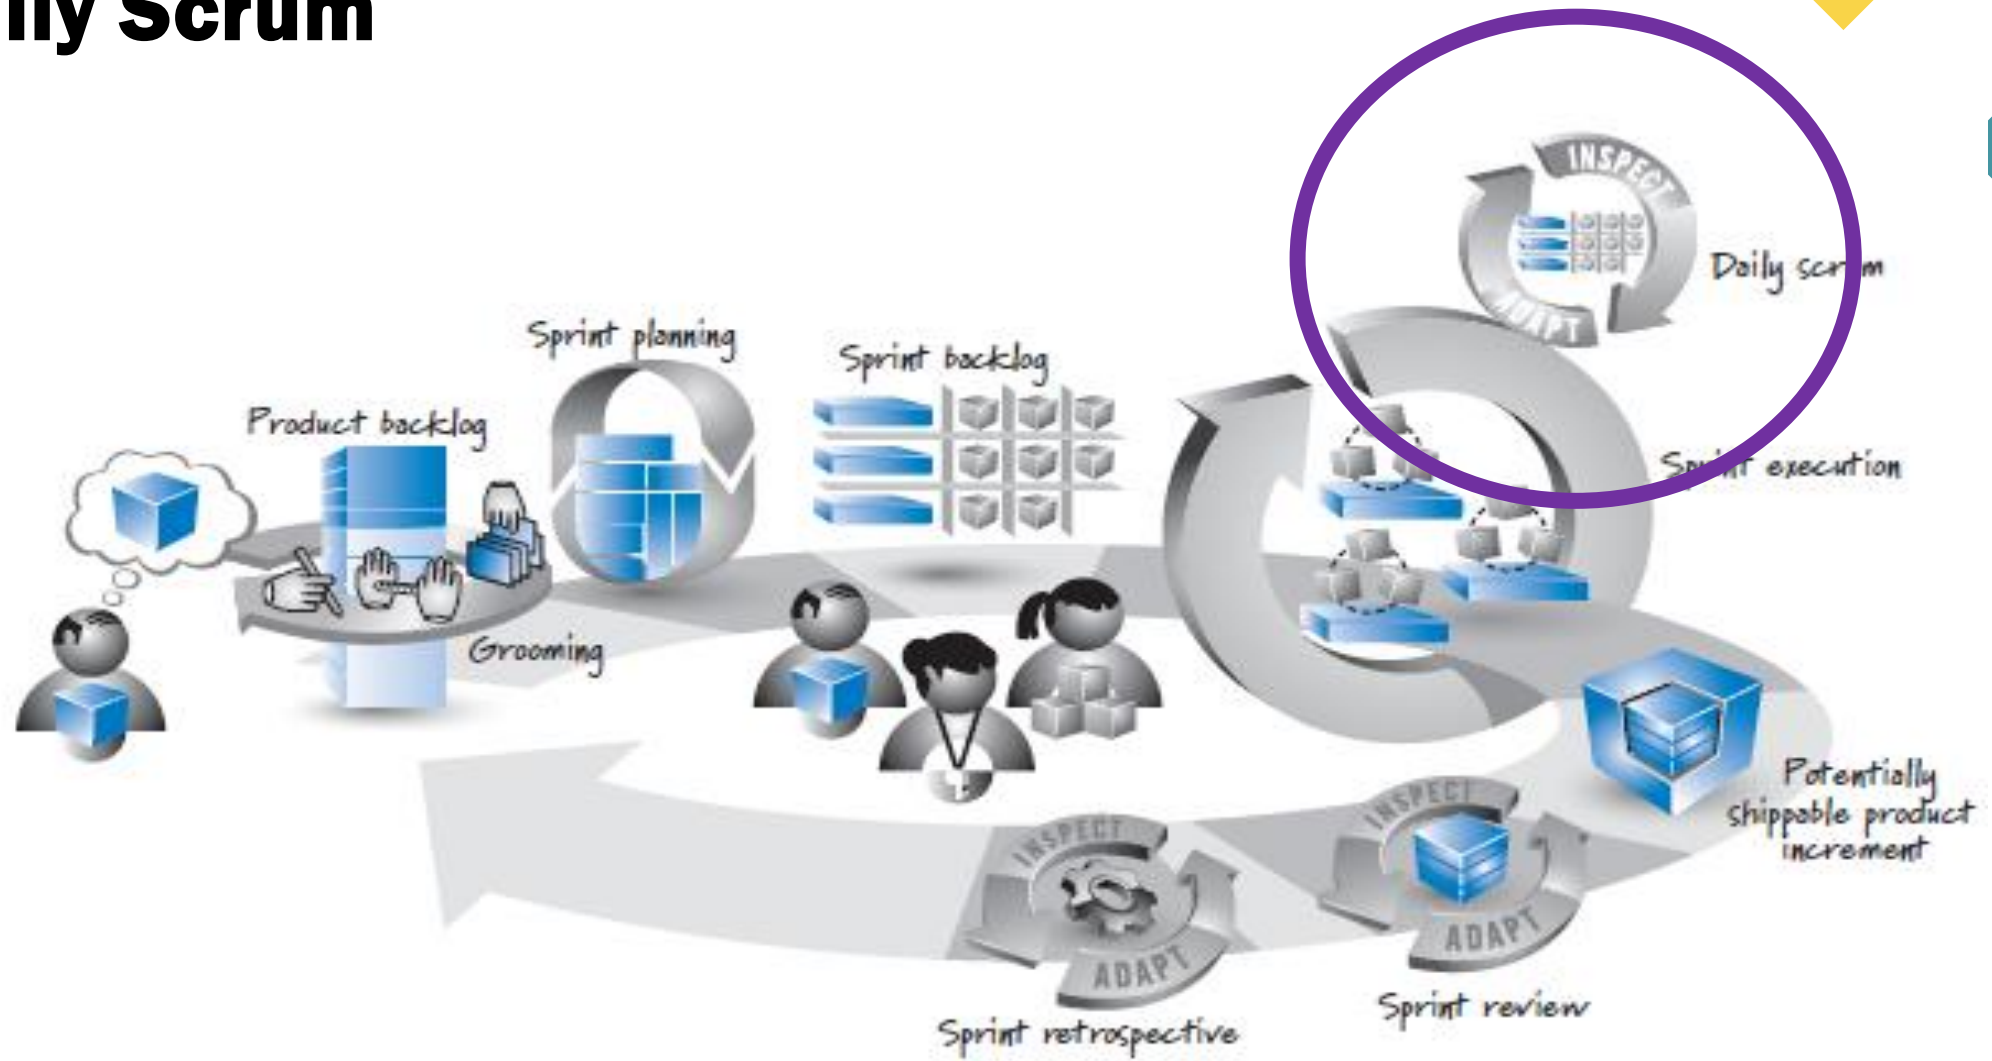

Daily Scrum

- Each day of the sprint, ideally at the same time, the development team hold a time-boxed (15 minutes or less) daily scrum

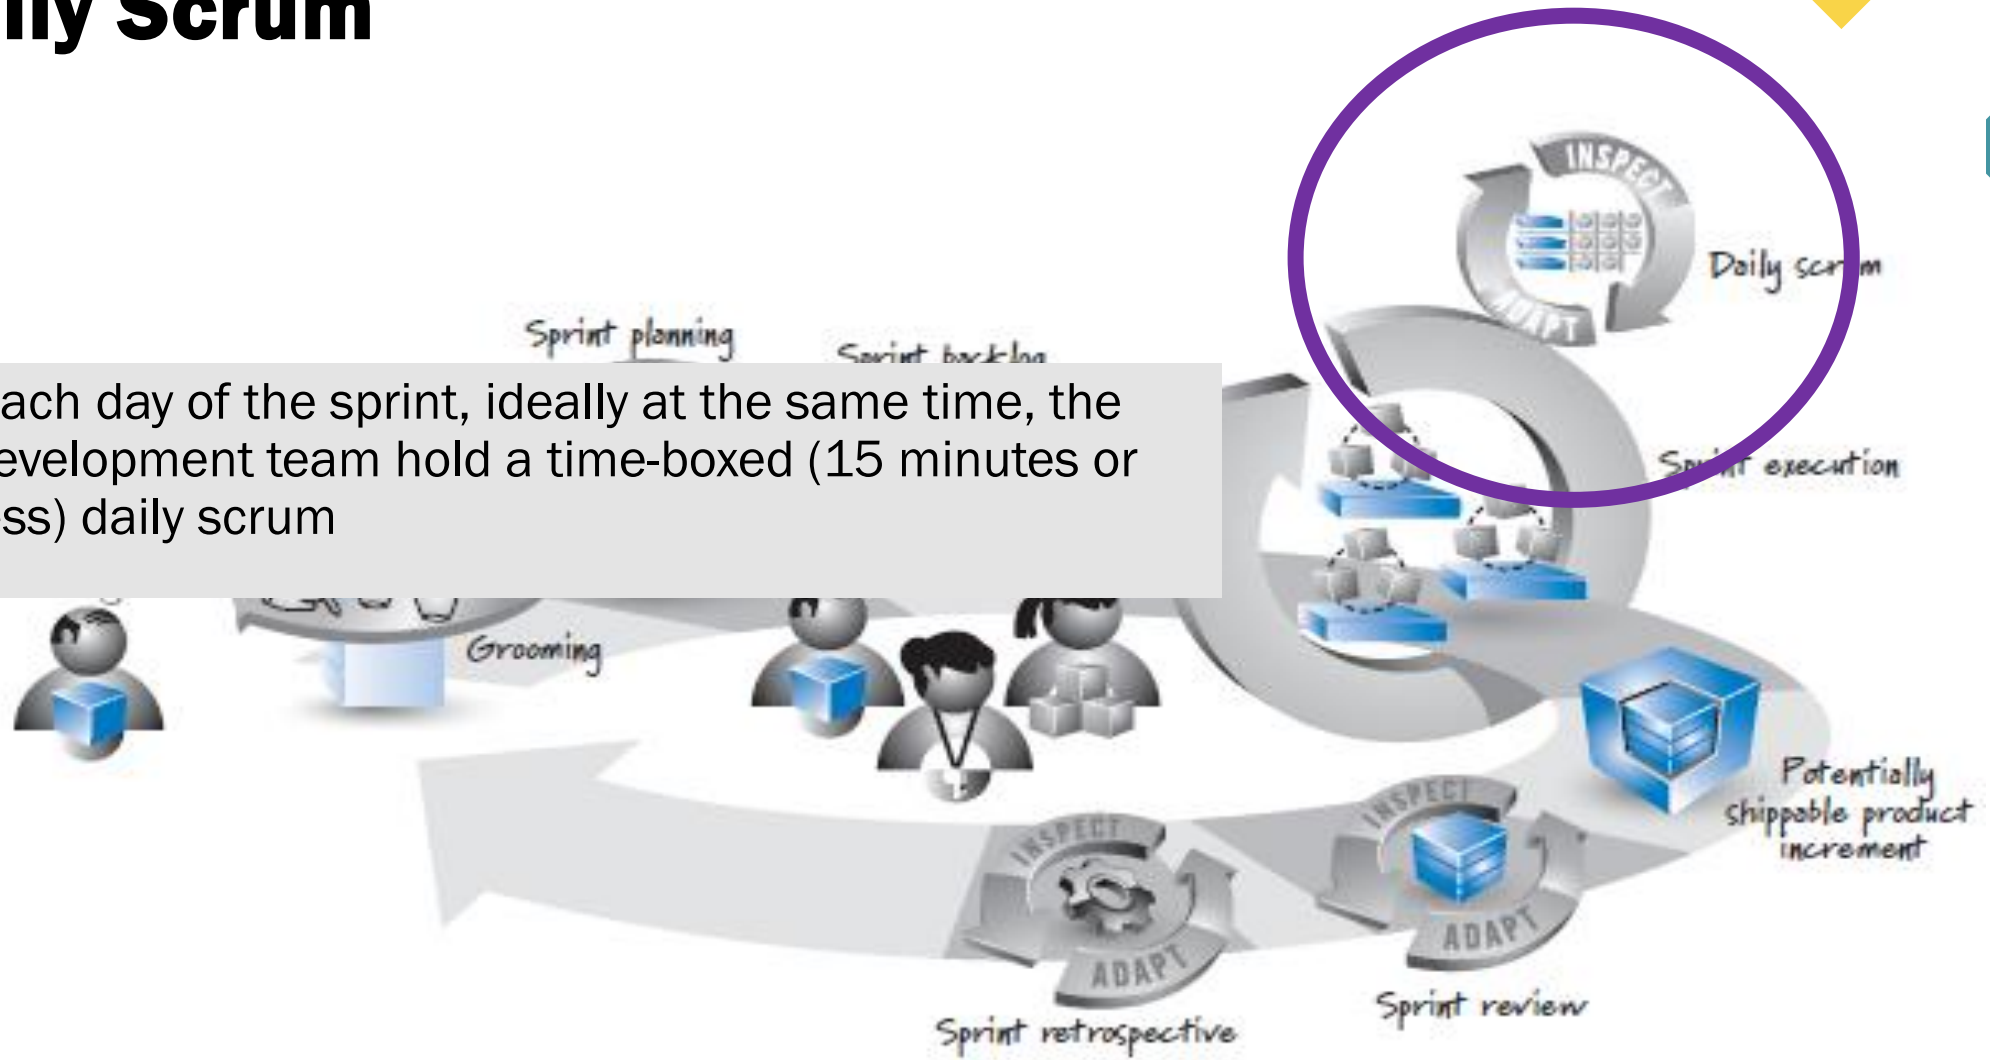


Definition of Done

- We refer to the sprint results as a potentially shippable product increment
- Potentially shippable = confidence that nothing more is needed
- Allows for feedback




Sprint Review

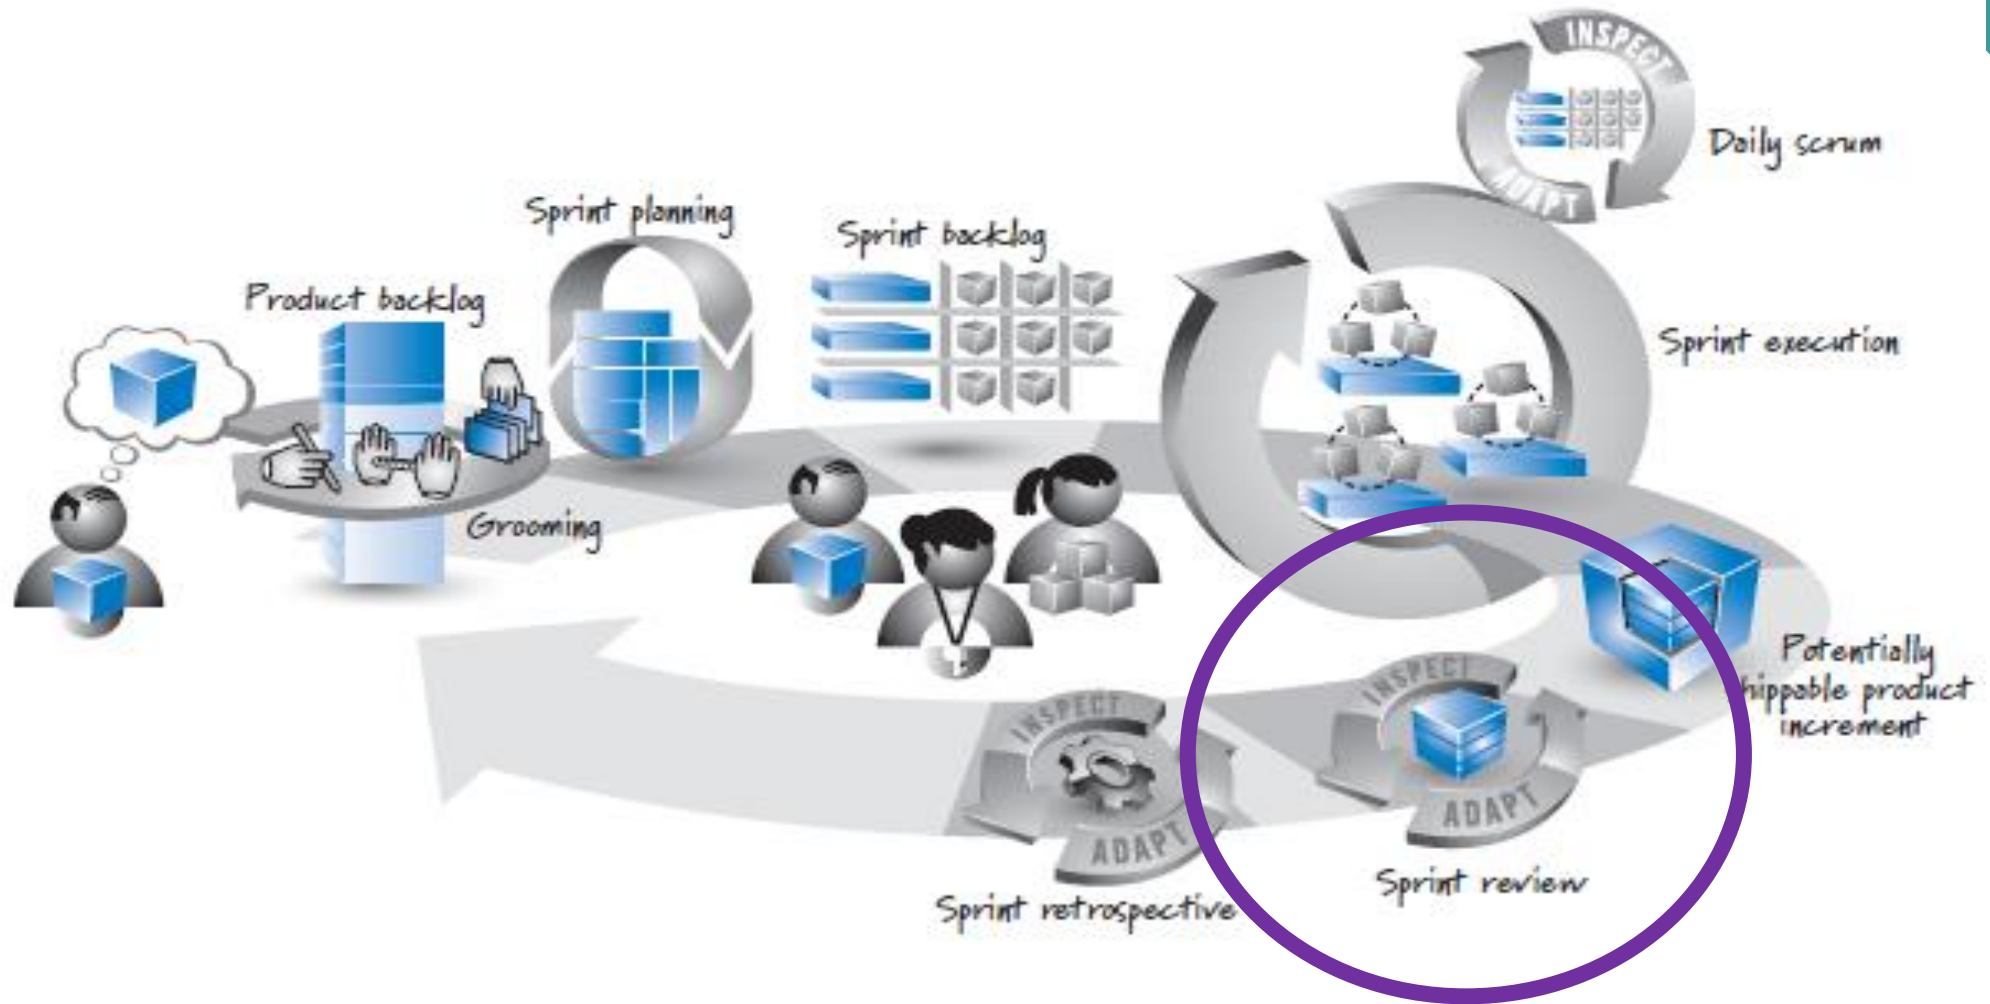


Sprint Review

- Comes at the end of the sprint, to inspect-and-adapt the product
- Likely involves others not on the sprint team
- Involves bidirectional information flow. The people who aren't on the Scrum team get to sync-up on the development effort and help guide its direction;
- At the same time, the Scrum team members gain a deeper appreciation for the business and marketing side of their product

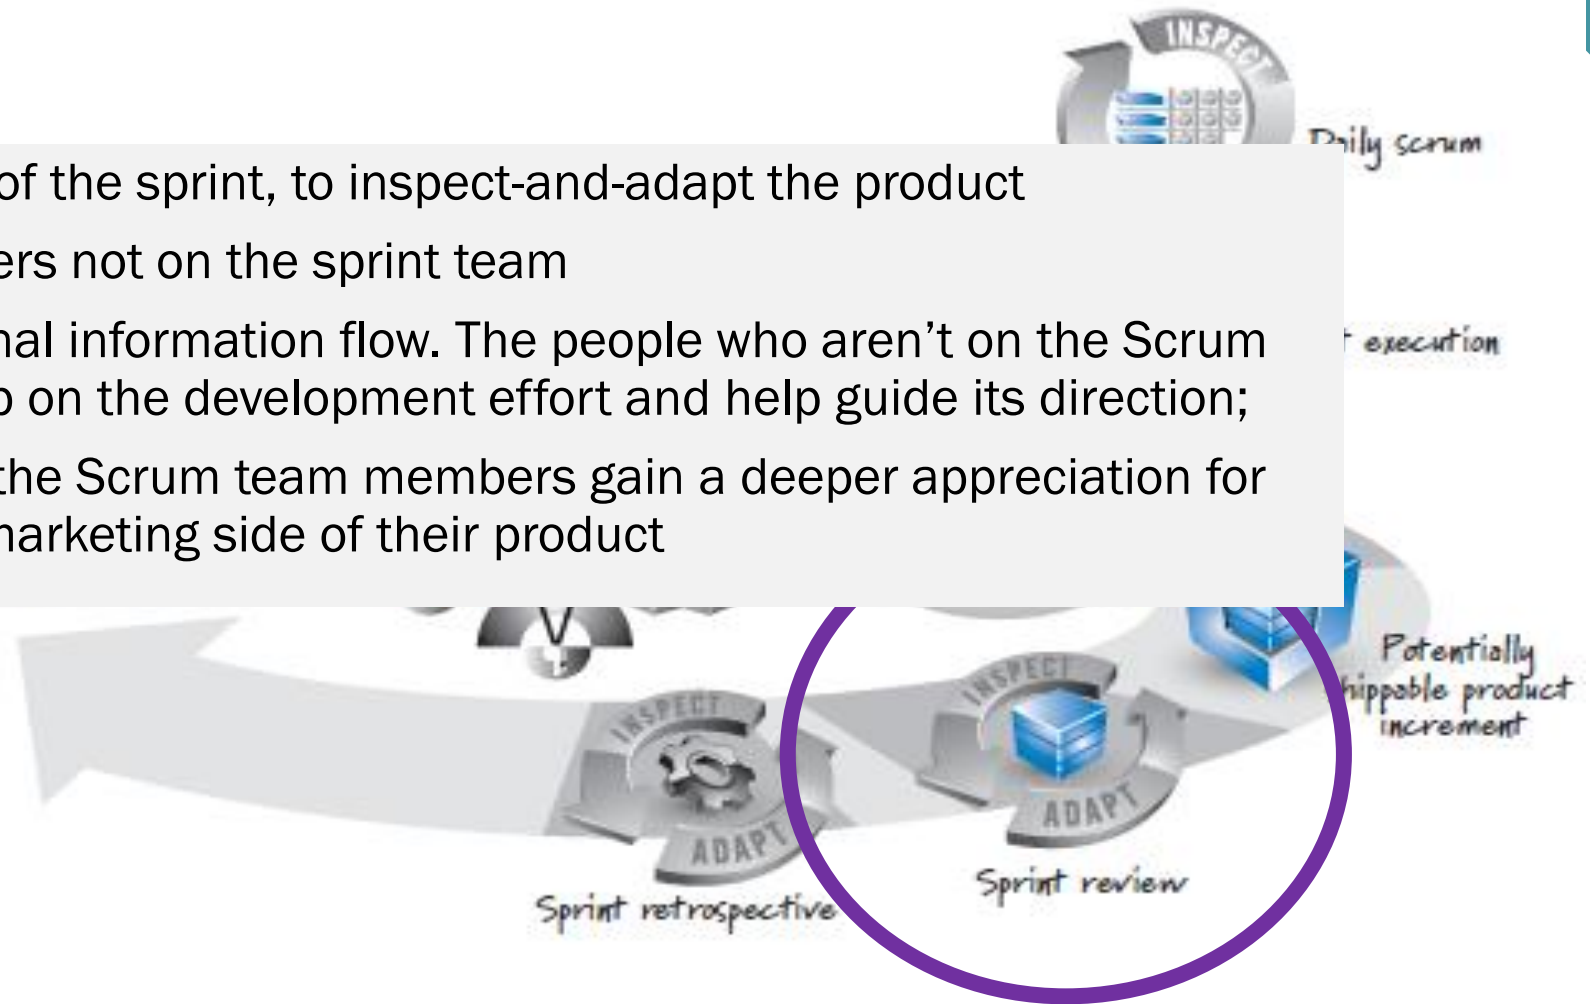

Sprint Retrospective

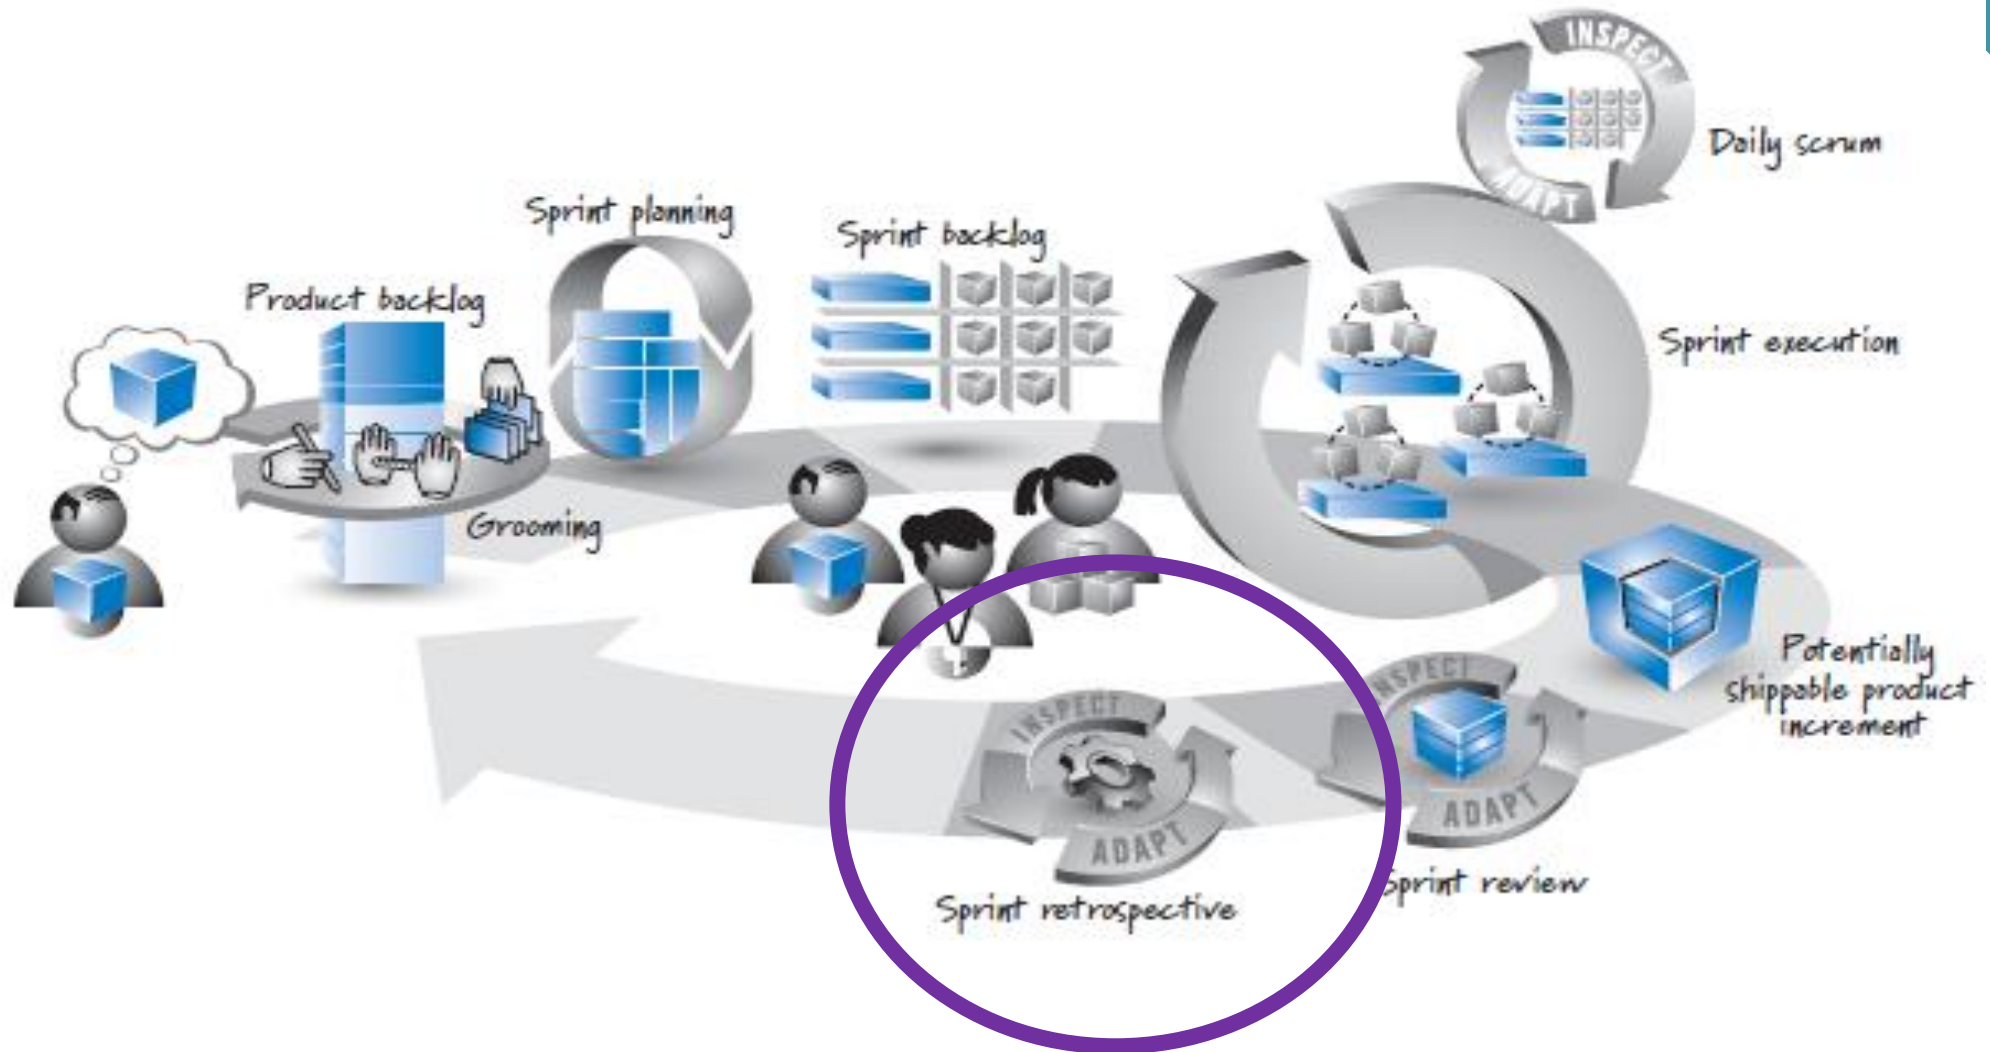

Sprint Retrospective

- Another inspect-and-adapt exercise at the end of a sprint: focused on process not product
- The whole team: PO, SM and DT all meet to discuss experience
- Decides process improvement actions for the next sprint

